

SE LAB-2

ATISHAY JAIN

PES1UG24CS097 B section

The screenshot displays the Jira interface for the 'Second Hand escrow marketplace' project. The left sidebar shows navigation options like 'For you', 'Recent', 'Starred', 'Apps', 'Plans', 'Spaces', 'Recent', 'More spaces', 'Recommended', 'Create a roadmap', 'Filters', 'Dashboards', 'Teams', 'Goals', 'Projects', and 'Customize sidebar'. The main content area shows the 'Backlog' view with a search bar and a filter button. The backlog is organized into a 'SCRUM Sprint 2' with 6 work items. The items are listed as follows:


Item ID	Item Name	Epic	Status
SCRUM-11	1.1 Create Product Listing	Epic 1: Product List...	To Do
SCRUM-13	2.1 Place Escrow Order	Epic 2: Escrow Ord...	To Do
SCRUM-14	2.2 Lock Payment in Escrow	Epic 2: Escrow Ord...	To Do
SCRUM-16	3.1 Submit Inspection Report	Epic 3: Inspection ...	To Do
SCRUM-17	4.1 Confirm Delivery & Sign Off	Epic 4: Delivery C...	To Do
SCRUM-18	4.2 Release Escrow Funds	Epic 4: Delivery C...	To Do

Below the sprint view, there is a 'Backlog' section with 3 work items:

Item ID	Item Name	Epic	Status
SCRUM-12	1.2 Browse & Search Listings	Epic 1: Product List...	To Do
SCRUM-15	2.3 Apply Promo Code	Epic 2: Escrow Ord...	To Do
SCRUM-19	5.1 Resolve Dispute & Freeze Funds	Epic 5: Dispute Re...	To Do

The screenshot displays the Jira interface for the 'Second Hand escrow marketplace' project, showing the 'Board' view. The left sidebar is the same as the previous screenshot. The main content area shows the 'Board' view with a search bar and a filter button. The board is organized into columns: 'To Do' (3 items), 'In Progress' (1 item), 'In Review' (0 items), and 'Done' (2 items). The items are listed as follows:

Column	Item ID	Item Name	Epic	Status
To Do	SCRUM-16	3.1 Submit Inspection Report	Epic 3: Inspection & Verification	To Do
	SCRUM-17	4.1 Confirm Delivery & Sign Off	Epic 4: Delivery Confirmation & Fu...	To Do
	SCRUM-18	4.2 Release Escrow Funds	Epic 4: Delivery Confirmation & Fu...	To Do
In Progress	SCRUM-14	2.2 Lock Payment in Escrow	Epic 2: Escrow Order & Payment	In Progress
Done	SCRUM-11	1.1 Create Product Listing	Epic 1: Product Listing & Discovery	Done
	SCRUM-13	2.1 Place Escrow Order	Epic 2: Escrow Order & Payment	Done

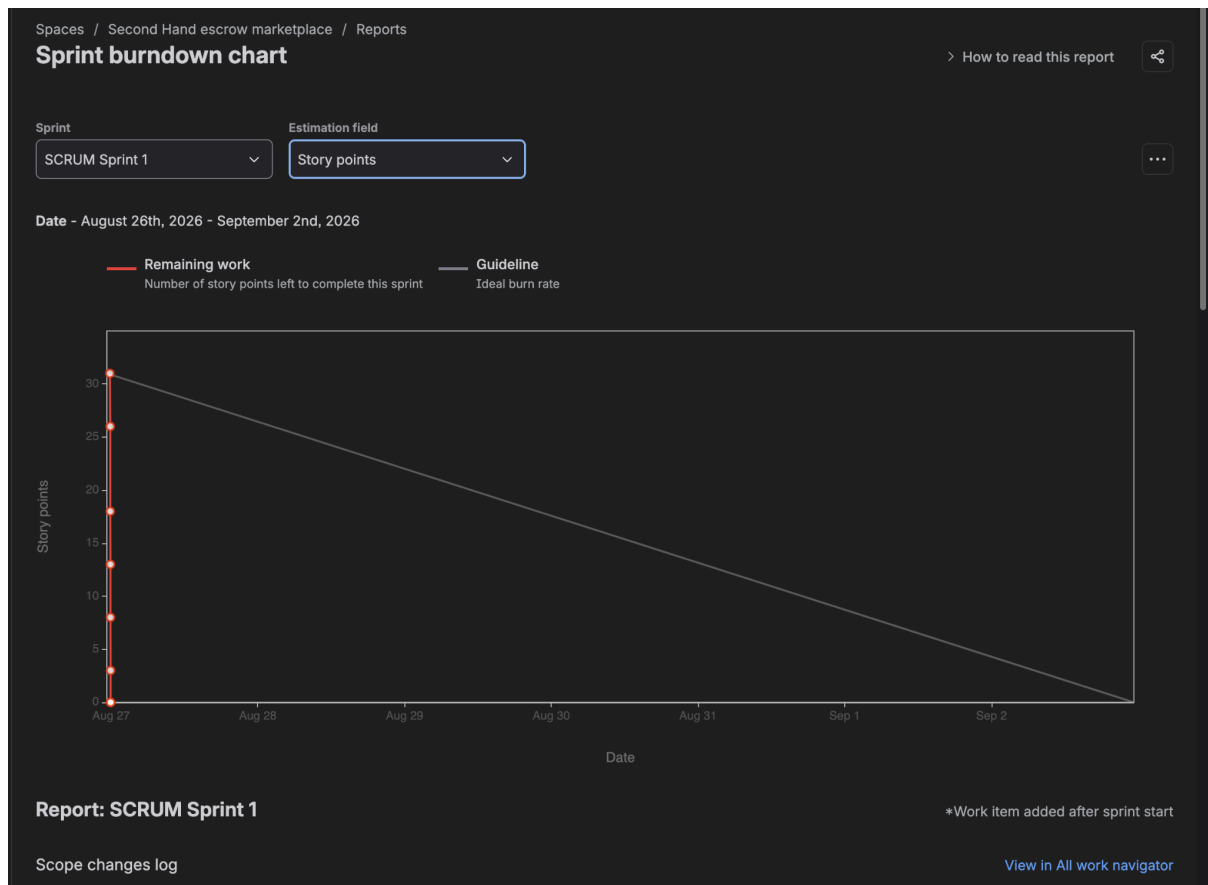

1. Did your estimations reflect the actual effort?

Not in a way that could be meaningfully tested. Story points were assigned up front using the Fibonacci scale based on perceived complexity — for example, Place Escrow Order (8 points) was rated highest because it touches payment locking and the Payment Gateway, while Apply Promo Code (2 points) was rated lowest as a small, optional add-on. However, because this was a simulated sprint rather than a real one, all six Sprint 1 items were moved to Done within a single session rather than worked on over the actual week. That means the point values were never tested against real elapsed effort. In a live team, the gap between a review's worth of "complete Place Escrow Order" (8 points) versus "add Apply Promo Code" (2 points) would only become clear once real hours were logged against each; here, the burndown chart shows the same instant completion for both, which is a limitation of the simulation rather than evidence the estimates were accurate.

2. Was your backlog well-prioritized?

Largely yes. The five High-priority stories — Create Product Listing, Place Escrow Order, Lock Payment in Escrow, Submit Inspection Report, and Confirm Delivery & Sign Off — form the minimum path a transaction needs to complete end-to-end, so putting them all in Sprint 1 was the right call. Release Escrow Funds was also included even though it depends directly on Confirm Delivery & Sign Off completing first, which in hindsight highlights a sequencing dependency the priority field alone doesn't capture. The Medium and Low items (Browse & Search Listings, Apply Promo Code, Resolve Dispute & Freeze Funds) were correctly deferred to Sprint 2, since a buyer can still complete a purchase without search/filtering or promo codes, and disputes are an edge case rather than the core flow. One thing worth reconsidering: Resolve Dispute & Freeze Funds protects real money and arguably deserved a higher priority than Browse & Search, even though it's a less frequent path.

3. How did your simulated sprint align with your plan?

All 6 planned Sprint 1 items (SCRUM-11, 13, 14, 16, 17, 18) reached Done, so scope-wise the sprint matched the plan exactly — nothing was descoped and nothing extra was pulled in. Where it diverged from a realistic sprint is pace: the board showed a natural in-flight state (3 To Do, 1 In Progress, 2 Done) partway through, but all items were completed well before the 1-week window actually closed. A real team spreading this work across 5 working days would show a more gradual progression through In Progress rather than clearing the board almost immediately, which is the main artificial aspect of simulating a sprint solo rather than with a team logging real work over time.

4. What insights did the burndown chart give about your team's capacity?

The chart shows all 31 story points dropping from remaining to zero on the very first day (Aug 27), while the grey guideline projects a smooth linear burn down to zero by Sep 2. In a real sprint, a drop this sharp this early would usually mean the team drastically underestimated how much they could do, or the work was already done before the sprint officially started — both are scope-planning red flags worth investigating. In this case it reflects the nature of a simulated, single-session sprint rather than genuine team capacity, but it's a useful illustration of exactly the pattern the lab describes: a burndown that falls in sharp steps rather than tracking the guideline signals that work wasn't paced steadily, and that the reported story points don't yet correspond to verified real-world effort. For Sprint 2, the more realistic approach would be to actually spread task transitions (To Do → In Progress → Done) across several days to get a burndown that tracks closer to the guideline.
